

PUMP TEST REPORT



Invoice Number:

Customer: Colgate

Job Number:

Fabrication

Pump Model: P1 4.0KW

Serial Number: 7101 001 - 25

Impeller Diameter: 140

Assembled By: tester1

Details

Motor Size: 3KW

Frequency: 50

Motor Speed: 2880

Pump Housing: 316 SS

Motor Volts: 380

Pump Connection: DIN

Motor Enclosure: IP55

Suction: 50

Mechanical Seal: TC/TC EPDM

Discharge: 40

Flush Arrangement: No

Hydraulic Test


Date of Test: 2025-03-17

Duration of Test: 1 HOUR

Test Medium: WATER

Tested By: tester1

| Test Data | Flowrate (l/h) | Pressure (bar) | Amperage |
|-----------|----------------|----------------|----------|
| Test 1 | 17912 | 2.85 | 6.19 |
| Test 2 | 12050 | 3.05 | 5.52 |
| Test 3 | 8078 | 3.05 | 5.2 |
| Test 4 | 4089 | 3.05 | 4.87 |
| Test 5 | 0 | 3.05 | 4.74 |

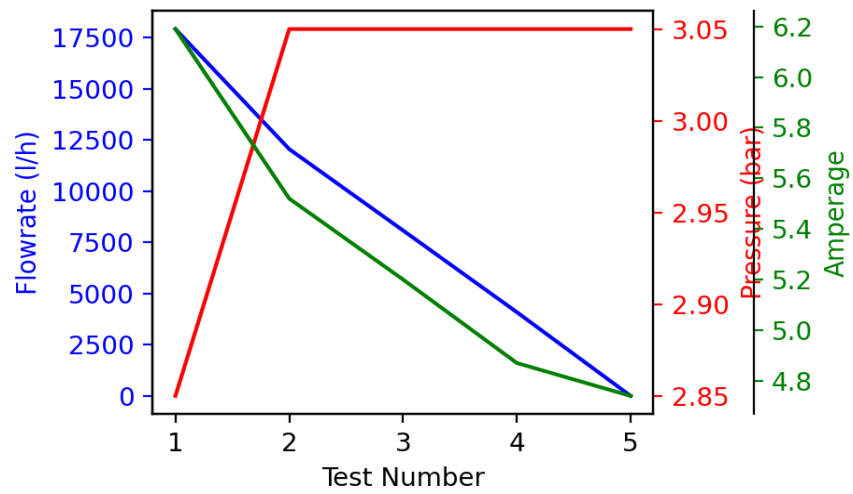

Approved By: TRAVIS MAIN
Date: 2025-03-17
