

## **PUMP TEST REPORT**


Invoice Number:	INV123
Customer:	Guth Durban
Job Number:	J0B456

FABRICATION		HYDRAULIC TEST	
Pump Model:	P1 3.0KW	Date of Test:	2025-03-18
Serial Number:	6101 002 - 25	Duration of Test:	1 HOUR
Impeller Diameter:	190	Test Medium:	WATER
Assembled By:	assembler1	Tested By:	assembler1

DETAILS				
Motor Size:	3.0KW	Frequency:	50	
Motor Speed:	2880	Pump Housing:	S/S 316	
Motor Volts:	380	Pump Connection:	DIN	
Motor Enclosure:	IP 55	Suction:	50	
Mechanical Seal:	TC/TC	Discharge:	40	
		Flush Arrangement:	No	

## **TEST RESULTS**

Test	Flowrate (L/h)	Pressure (bar)	Amperage (A)
Test 1	17912	2.85	6.19
Test 2	12050	3.05	5.52
Test 3	8078	3.05	5.2
Test 4	4089	3.05	4.87
Test 5	0	3.05	4.74

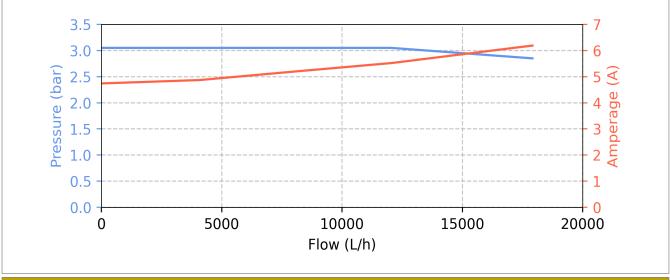

APPROVAL				
Approved By:	approver1			
Date:	2025-03-18			
