

## **PUMP TEST REPORT**


Invoice Number:	
Customer:	Lancewood
Job Number:	

FABRICATION		HYDRAULIC TEST	
Pump Model:	P1 1.1KW	Date of Test:	2025-03-20
Serial Number:	4101 002 - 25	Duration of Test:	1 hour
Impeller Diameter:	180	Test Medium:	water
Assembled By:	tester1	Tested By:	tester1

DETAILS			
Motor Size:	4 kw	Frequency:	50
Motor Speed:	2880	Pump Housing:	s/s 316
Motor Volts:	380	Pump Connection:	din
Motor Enclosure:	ip 55	Suction:	50
Mechanical Seal:	tc/tc	Discharge:	40
		Flush Arrangement:	No

## **TEST RESULTS**

Test	Flowrate (L/h)	Pressure (bar)	Amperage (A)
Test 1	17912	2.85	6.19
Test 2	12050	3.05	5.52
Test 3	8078	3.05	5.2
Test 4	4089	3.05	4.87
Test 5	0	3.05	4.74

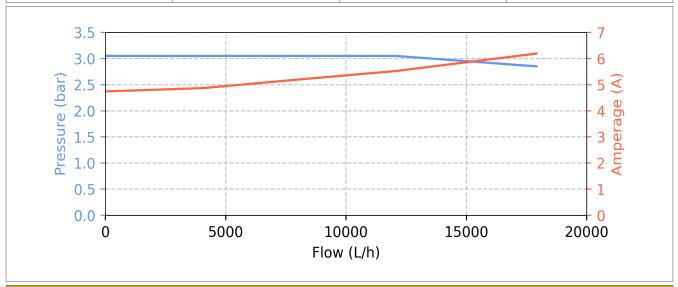

APPROVAL				
Approved By:	approver1			
Date:	2025-03-20			
