

## **PUMP TEST REPORT**


Invoice Number:	123
Customer:	SSSPI
Job Number:	1234

FABRICATION		HYDRAULIC TEST	
Pump Model:	P1 2.2KW	Date of Test:	2025-03-17
Serial Number:	5101 003 - 25	Duration of Test:	1 hour
Impeller Diameter:	180	Test Medium:	WATER
Assembled By:	tester1	Tested By:	tester1

DETAILS				
Motor Size:	12	Frequency:	121	
Motor Speed:	12	Pump Housing:	122	
Motor Volts:	12	Pump Connection:	12	
Motor Enclosure:	121	Suction:	321	
Mechanical Seal:	212	Discharge:	12	
		Flush Arrangement:	No	

## **TEST RESULTS**

Test	Flowrate (L/h)	Pressure (bar)	Amperage (A)
Test 1	17912	2.85	6.19
Test 2	12050	3.05	5.52
Test 3	8078	3.05	5.2
Test 4	4089	3.05	4.87
Test 5	0	3.05	4.74

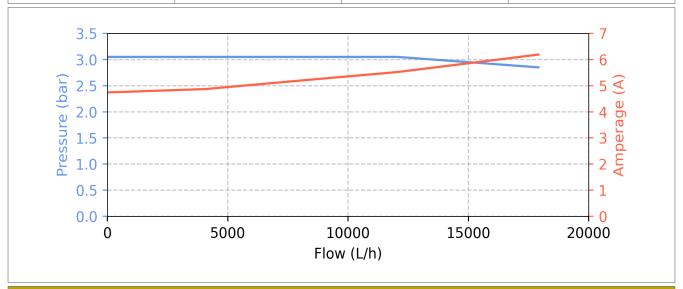

APPROVAL				
Approved By:	TRAVIS MAIN			
Date:	2025-03-17			
