

PUMP TEST REPORT


Invoice Number:	123
Customer:	Leonards Wife
Job Number:	3

FABRICATION		HYDRAULIC TEST	
Pump Model:	P1 4.0KW	Date of Test:	2025-03-17
Serial Number:	7101 002 - 25	Duration of Test:	1 HOUR
Impeller Diameter:	180	Test Medium:	WATER
Assembled By:	tester1	Tested By:	tester1

DETAILS				
Motor Size:	4KW	Frequency:	50	
Motor Speed:	2880	Pump Housing:	SS 316	
Motor Volts:	380	Pump Connection:	DIN	
Motor Enclosure:	IP 55	Suction:	65	
Mechanical Seal:	TC/TC	Discharge:	50	
		Flush Arrangement:	No	

TEST RESULTS

Test	Flowrate (L/h)	Pressure (bar)	Amperage (A)
Test 1	18000	3	7
Test 2	15000	2.8	6
Test 3	12000	3.5	5
Test 4	10000	3.8	4
Test 5	9000	3.9	3

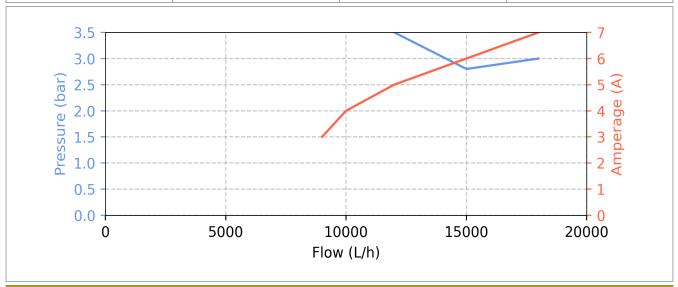

APPROVAL					
Approved By:	TRAVIS MAIN				
Date:	2025-03-17				
